



PM Fair 2022, 7th October

The Royal Museum for Central Africa
Tervuren, Belgium




Presentation

**Three things you might be missing
in your PM framework**



Pavel Jonis

Project Management Consultant



The Problem(s)

**Project Managers
are too distant
from Business**

**Little to no
discussion in a
start driven culture**

**A growing need to
implement PM as a
standard**

Criteria



**Implemented
easily and quickly**



**Creates
measurable value**



**Easy to sell to
stakeholders**

The background features a complex, abstract pattern of overlapping, three-dimensional geometric shapes in shades of teal and white. The shapes create a sense of depth and movement, resembling a stylized architectural or digital landscape.

BUSINESS VALUE

Accountability Mindset


*“Using the traditional model, project managers have focused far too much on **inputs and outputs** (planning, estimation, cost, time, scope, risk management) and not nearly enough on outcomes and value (purpose, rationale, benefits, impact, and strategy).*

*It hasn't mattered much to them what happens before or after their projects are complete— they've concerned themselves with deliverables, the idea being that if they can complete their projects on time, on budget, and on scope, then the promised **benefits will... just happen**”.*

PROJECT ECONOMY
Antonio Nieto-Rodriguez
(HBR, Nov-Dec, 2021)



P3.express

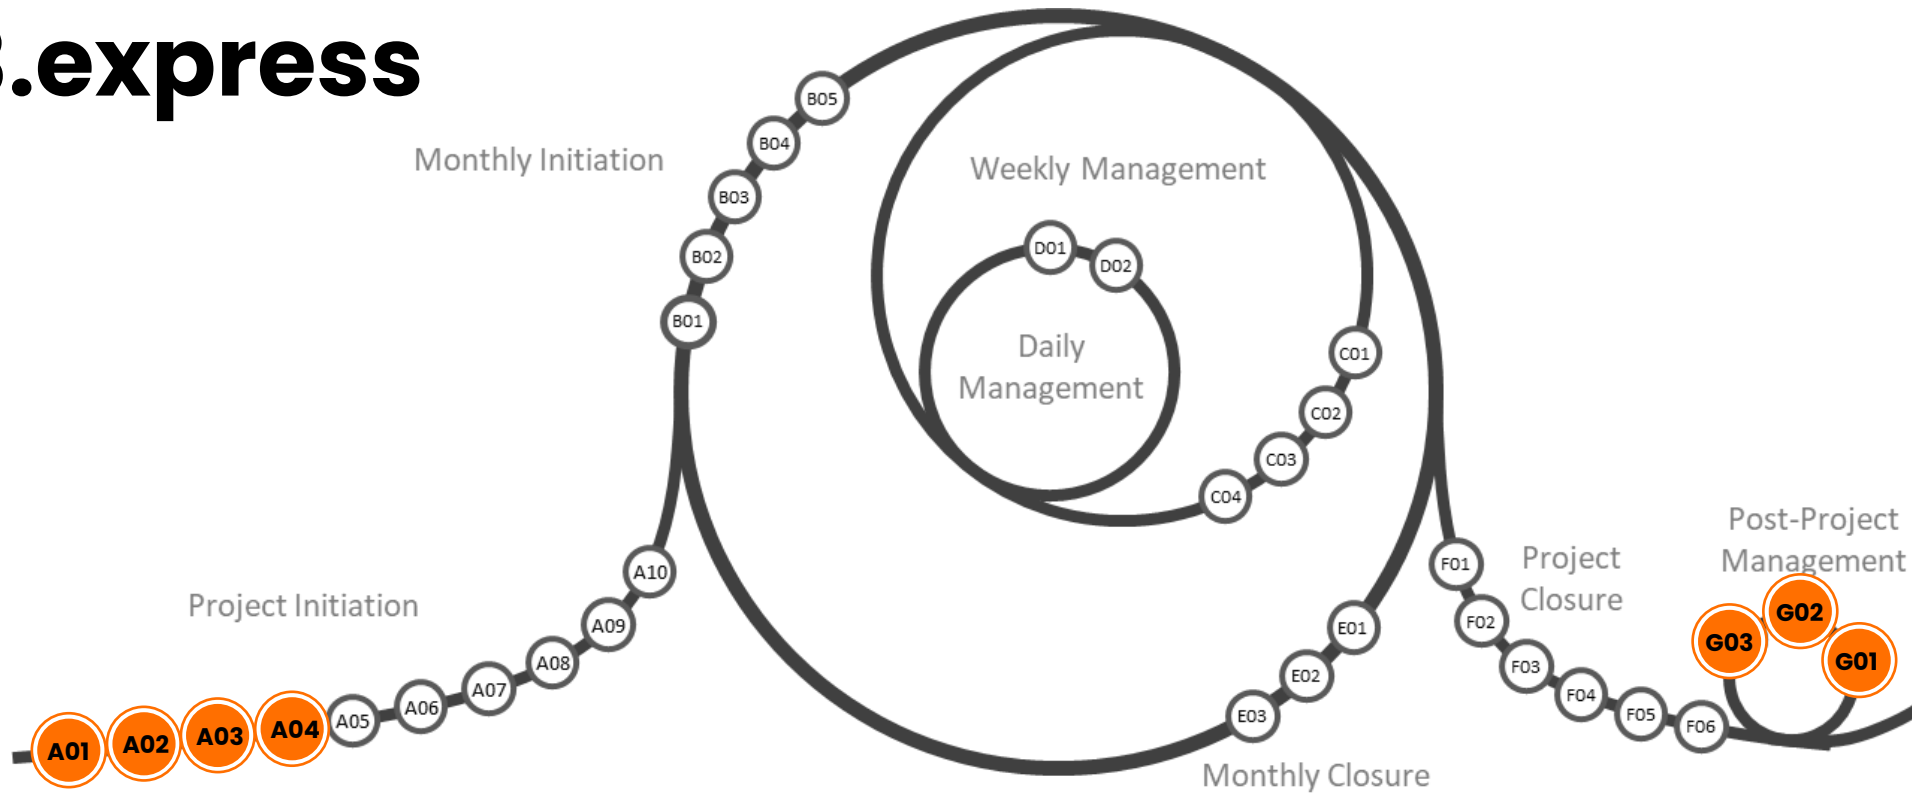

- A01** Appoint the sponsor
- A02** Appoint PM
- A03** Appoint Key Team Members
- A04** Describe the Project

PROJECT INITIATION

- G01** Evaluate the Benefits
- G02** Generate New Ideas
- G03** Conduct a Focused Communication

POST-PROJECT INITIATION

PROJECT NAME



Project Purpose



Benefits

Stakeholders

Product and quality
requirements

Costs and
timeline

PROJECT INITIATION



- ▶ Competence
- ▶ Business Understanding
- ▶ Vision -> Execution
- ▶ Sense of Control
- ▶ Accountability

POST-PROJECT



- ▶ Surviving Victory
- ▶ Measured Value
- ▶ Execution -> Vision
- ▶ Lessons Learned
- ▶ Sense of Accomplishment






CONTINUOUS IMPROVEMENT

Raising the Floor

P3.express

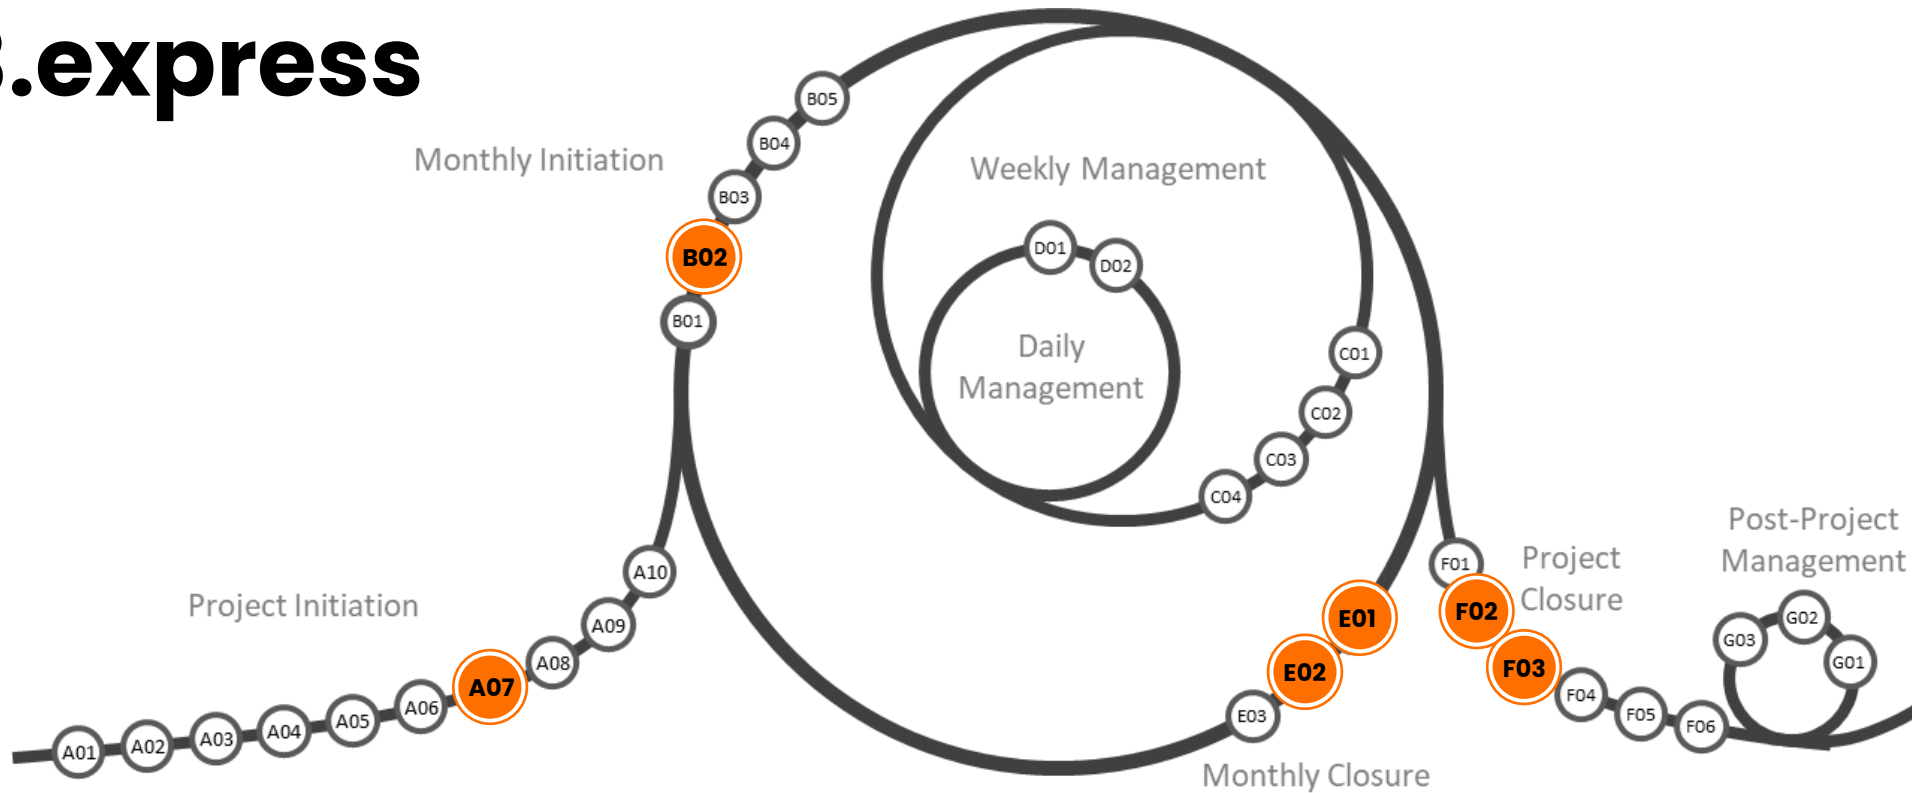

A07

Have Project Initiation Peer Reviewed

PROJECT INITIATION

B02

Have the Monthly Cycle Reviewed

MONTHLY INITIATION

E01

Evaluate Stakeholder Satisfaction

MONTHLY CLOSURE

E02

Capture Lessons Learned and Plan for Improvements

F02


Evaluate Stakeholder Satisfaction

PROJECT CLOSURE


F03

Have the Closing Activity Peer-Reviewed

Peer Review Benefits



**Creates a need for
organizational Way
of Working**



**Project
Management
Factory**



**Increases
performance**

The background features a complex, three-dimensional geometric pattern of teal and white lines that create a sense of depth and movement, resembling a stylized architectural or digital structure.

PRACTICALITY AS A VALUE


Apply Now




COMMUNITY



TOOLS



**EASY TO
EXPLAIN**



Thank you!

Pavel Jonis

Project Management Consultant

paveljonis@gmail.com





PM Fair 2022, 7th October

The Royal Museum for Central Africa
Tervuren, Belgium



**A big “Thank You!” ... to our Sponsors,
without you this wouldn’t be possible!**



PROSOURCE
powered by **Sisu:**

MindManager®

COLRUYT GROUP | IT

The Bayard Partnership
Making a difference at work and in the community

BOOST YOUR SCRUM

P3.express
The minimalist project management system

PSO Belgium sprl



pmi-belgium.be

info contact: sponsorship@pmi-belgium.be

www.pmfair.org

